

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Notice of Operations at Beatrice Offshore Wind Farm

Work Planned for the Period 14-05-2018 to 20-05-2018

Construction of the Beatrice Offshore Wind Farm commenced on the 1st of April 2017.

This notice will be updated weekly giving information on the progress and resources involved in the offshore project. The intention is to give an overview of activities and vessels involved. Should anyone have questions regarding the operations, we kindly ask you to put them forward well in advance.

Beatrice Offshore Windfarm Limited (BOWL) is developing the Beatrice Offshore Wind Farm in the 'Outer' Moray Firth on the north-western point of the Smith Bank, approximately 7 nm off the Caithness coastline. The development site will cover an approximate area of up to 130km² and will consist of 84 7MW offshore wind turbines (with a total capacity of 588MW) and two HVAC Offshore Transformer Modules (OTM). Water depths in the area range from approximately 38m below LAT in the south of the field to 60m below LAT in the north. The generated power will be transmitted to the grid via two subsea export / transmission cables with a landfall near Portgordon to the south of the field and grid connection at Blackhillock. The transmission cables will cover a route of approximately 38 nm from the wind farm boundary back to the landfall. The Beatrice Offshore Wind Farm development area is highlighted in red below, the OFTW cable corridor in black.

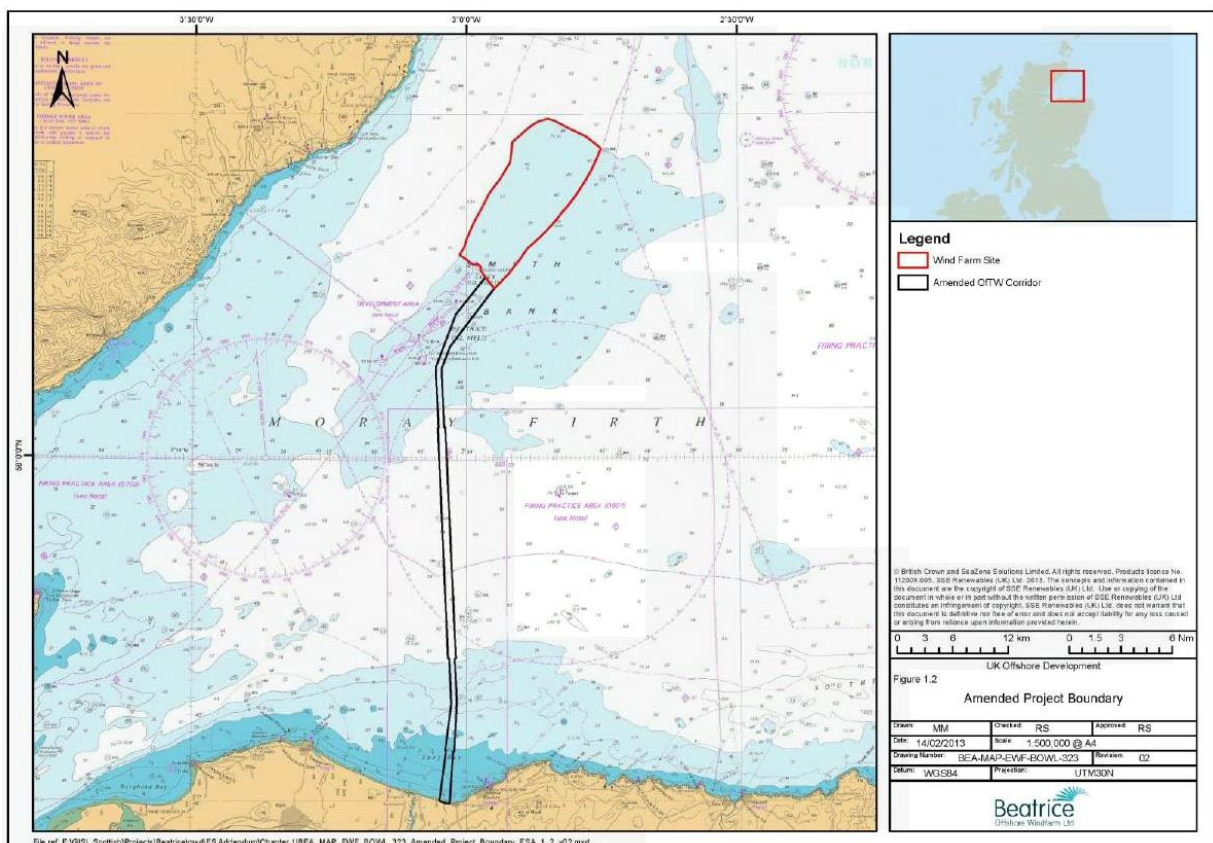


Fig. 1 Beatrice Offshore Wind Farm Location

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

1. Contact Details for Marine Coordination

The following contact can provide more information if required. Please note that specific queries can also be addressed to the relevant vessel or shore based representative.

Telephone Number	+44 (0) 3302 020329
Emergency Contact (24/7)	+44 (0) 7342 028207
Email for Marine Coordinator	mc.bowl@sse.com
Address	Unit 1 Harbour Office Wick Caithness KW1 5HA

2. Ongoing Operations

2.1 Beatrice Offshore Wind Farm Jacket Installation Campaign

Project:	Jacket Installation Campaign (See Notice to Mariners) NTM-032 Rev01
Contractor:	SHL
Contract Purpose:	To install WTG & OTM Jackets at completed piled locations within the construction site.
Area:	BOWL Construction Site: Jacket Locations (See Fig. 2 Table1)
Deployment Dates:	08 August 2017 – September 2018
Deployment Vessels:	HLV Oleg Strashnov, Smit Sentosa, AHT Maersk Trader, Britoil 120, Pegasus, Smit Seraya, Bremen Fighter, Kamarina, Centaurus, VOS Prelude, Fairplay-33, Bremen Fighter, Rix Lion, Rix Panther.
Equipment:	HLV equipment, Pile cleaning equipment, Grouting equipment.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

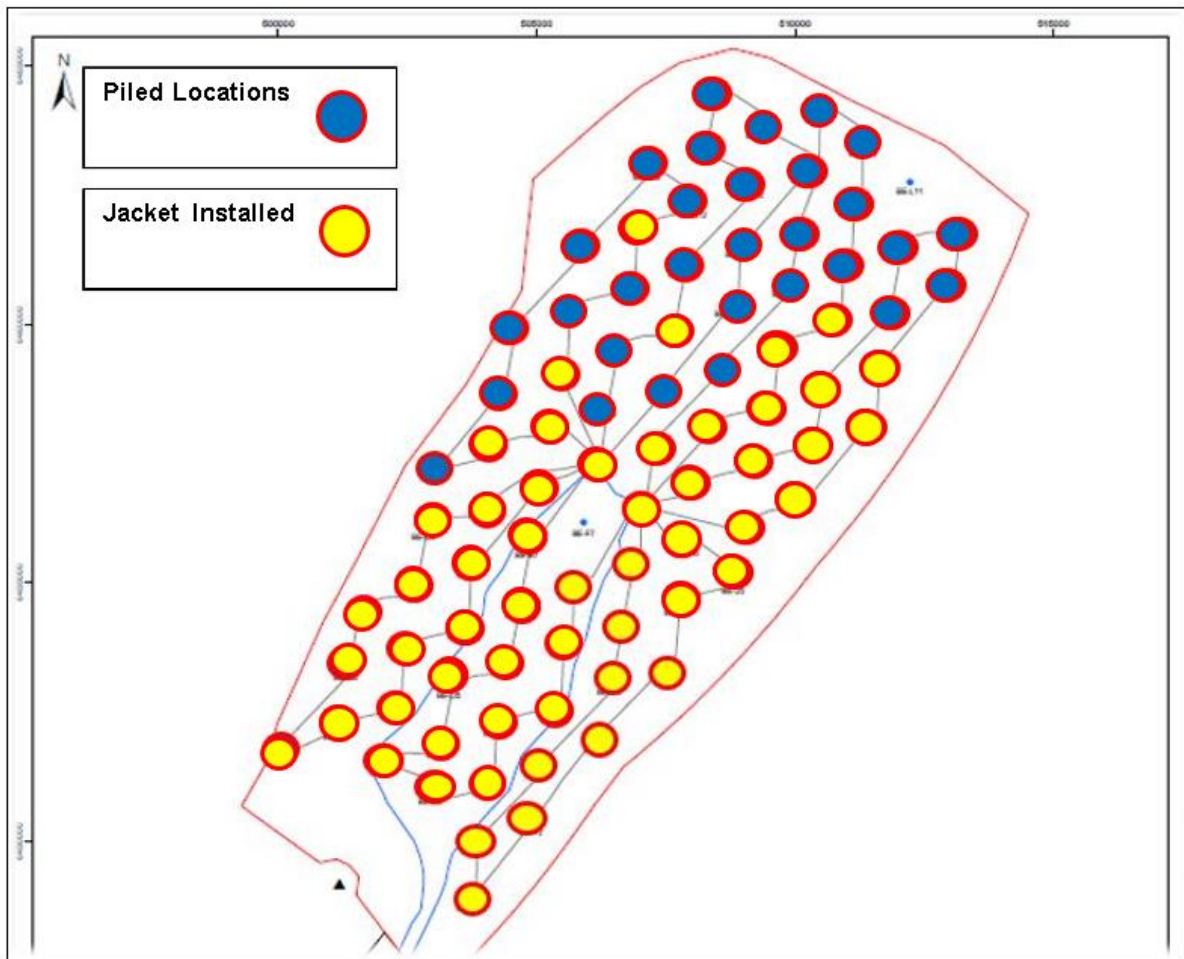


Fig. 2 Pile installation completed at 86 Locations

Foundation installation completed at 55 Locations

Table 1 - WTG and OTM Location Coordinates

Location ID	Latitude WGS84	Longitude WGS84	Piling Complete	Jacket installed
BE-A5	58° 12.471' N	002° 59.996' W	14.07.2017	21.04.2018
BE-B5	58° 12.687' N	002° 58.873' W	12.07.2017	23.03.2018
BE-B6	58° 13.308' N	002° 58.664' W	16.06.2017	22.02.2018
BE-B7	58° 13.929' N	002° 58.456' W	18.07.2017	20.02.2018
BE-C4	58° 12.307' N	002° 57.948' W	23.05.2017	13.12.2017
BE-C5	58° 12.902' N	002° 57.749' W	11.07.2017	09.02.2018
BE-C6	58° 13.524' N	002° 57.541' W	10.07.2017	08.02.2018
BE-C7	58° 14.144' N	002° 57.332' W	15.06.2017	01.09.2017
BE-C8	58° 14.766' N	002° 57.124' W	17.07.2017	20.01.2018
BE-C9	58° 15.386' N	002° 56.915' W	28.08.2017	
BE-D3	58° 11.995' N	002° 57.002' W	21.05.2017	12.12.2017
BE-D4	58° 12.497' N	002° 56.834' W	22.06.2017	14.12.2017

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Location ID	Latitude WGS84	Longitude WGS84	Piling Complete	Jacket installed
BE-D5	58° 13.117' N	002° 56.626' W	26.05.2017	21.01.2018
BE-D6	58° 13.739' N	002° 56.417' W	13.06.2017	31.08.2017
BE-D7	58° 14.359' N	002° 56.209' W	31.05.2017	18.01.2018
BE-D8	58° 14.981' N	002° 55.999' W	02.06.2017	20.12.2017
BE-D9	58° 15.602' N	002° 55.790' W	16.07.2017	21.09.2017
BE-D10	58° 16.223' N	002° 55.582' W	31.08.2017	
BE-D11	58° 16.844' N	002° 55.373' W	13.08.2017	
BE-E1	58° 10.900' N	002° 56.256' W	10.04.2017	01.09.2017
BE-E2	58° 11.470' N	002° 56.128' W	14.04.2017	16.08.2017
BE-E3	58° 12.090' N	002° 55.920' W	19.04.2017	02.12.2017
BE-E4	58° 12.712' N	002° 55.710' W	02.07.2017	20.09.2017
BE-E5	58° 13.333' N	002° 55.502' W	19.05.2017	03.02.2018
BE-E6	58° 13.954' N	002° 55.293' W	18.05.2017	24.08.2017
BE-E7	58° 14.575' N	002° 55.084' W	01.06.2017	25.08.2017
BE-E8	58° 15.196' N	002° 54.875' W	30.05.2017	18.12.2017
BE-E9	58° 15.817' N	002° 54.665' W	15.07.2017	21.09.2017
BE-E10	58° 16.438' N	002° 54.456' W	01.09.2017	08.05.2018
BE-E11	58° 17.059' N	002° 54.247' W	19.09.2017	
BE-E12	58° 17.680' N	002° 54.037' W	14.08.2017	
BE-F2	58° 11.685' N	002° 55.005' W	03.07.2017	06.09.2017
BE-F3	58° 12.306' N	002° 54.796' W	17.04.2017	07.09.2017
BE-F4	58° 12.927' N	002° 54.588' W	04.07.2017	19.09.2017
BE-F5	58° 13.548' N	002° 54.378' W	17.05.2017	14.09.2017
BE-F6	58° 14.168' N	002° 54.169' W	11.05.2017	11.09.2017
BE-F8 (OTM2)	58° 15.411' N	002° 53.750' W	08.04.2017	25.04.2018
BE-F9	58° 16.031' N	002° 53.540' W	22.09.2017	
BE-F10	58° 16.653' N	002° 53.330' W	20.09.2017	
BE-F11	58° 17.274' N	002° 53.120' W	07.09.2017	
BE-F12	58° 17.894' N	002° 52.911' W	05.07.2017	13.05.2018
BE-F13	58° 18.516' N	002° 52.701' W	10.09.2017	
BE-G3	58° 12.544' N	002° 53.726' W	28.05.2017	15.08.2017
BE-G4	58° 13.142' N	002° 53.464' W	17.06.2017	08.09.2017
BE-G5	58° 13.762' N	002° 53.254' W	10.05.2017	09.09.2017
BE-G6	58° 14.384' N	002° 53.044' W	06.05.2017	20.08.2017
BE-G7 (OTM1)	58° 15.004' N	002° 52.834' W	03.04.2017	06.02.2018
BE-G8	58° 15.625' N	002° 52.625' W	07.07.2017	10.09.2017
BE-G9	58° 16.247' N	002° 52.415' W	04.11.2017	
BE-G10	58° 16.867' N	002° 52.204' W	21.09.2017	30.04.2018
BE-G11	58° 17.488' N	002° 51.994' W	20.08.2017	
BE-G12	58° 18.109' N	002° 51.784' W	18.08.2017	
BE-G13	58° 18.730' N	002° 51.574' W	13.09.2017	
BE-G14	58° 19.351' N	002° 51.362' W	14.09.2017	
BE-H4	58° 13.356' N	002° 52.339' W	19.06.2017	13.08.2017
BE-H5	58° 13.977' N	002° 52.130' W	20.06.2017	27.08.2017
BE-H6	58° 14.598' N	002° 51.920' W	20.04.2017	21.08.2017

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Location ID	Latitude WGS84	Longitude WGS84	Piling Complete	Jacket installed
BE-H7	58° 15.219' N	002° 51.709' W	08.07.2017	11.05.2018
BE-H8	58° 15.840' N	002° 51.499' W	06.05.2017	13.09.2017
BE-H9	58° 16.461' N	002° 51.289' W	15.11.2017	
BE-H10	58° 17.082' N	002° 51.079' W	27.10.2017	
BE-H11	58° 17.703' N	002° 50.867' W	10.10.2017	
BE-H12	58° 18.324' N	002° 50.657' W	09.09.2017	
BE-H13	58° 18.944' N	002° 50.446' W	07.10.2017	
BE-J5	58° 14.192' N	002° 51.005' W	04.05.2017	26.08.2017
BE-J6	58° 14.812' N	002° 50.795' W	21.06.2017	25.03.2018
BE-J7	58° 15.433' N	002° 50.585' W	06.08.2017	14.05.2018
BE-J8	58° 16.055' N	002° 50.373' W	12.06.2017	22.12.2017
BE-J9	58° 16.675' N	002° 50.163' W	04.08.2017	
BE-J10	58° 17.296' N	002° 49.952' W	03.12.2017	
BE-J11	58° 17.917' N	002° 49.741' W	26.08.2017	
BE-J12	58° 18.538' N	002° 49.530' W	27.08.2017	
BE-J13	58° 19.159' N	002° 49.319' W	08.10.2017	
BE-K6	58° 15.027' N	002° 49.669' W	07.08.2017	24.12.2017
BE-K7	58° 15.648' N	002° 49.459' W	08.08.2017	30.12.2017
BE-K8	58° 16.269' N	002° 49.247' W	31.07.2017	27.04.2018
BE-K9	58° 16.890' N	002° 49.036' W	05.08.2017	29.04.2018
BE-K10	58° 17.510' N	002° 48.825' W	21.08.2017	
BE-K11	58° 18.131' N	002° 48.614' W	25.08.2017	
BE-K12	58° 18.752' N	002° 48.403' W	09.10.2017	
BE-L7	58° 15.862' N	002° 48.333' W	09.08.2017	01.01.2018
BE-L8	58° 16.482' N	002° 48.122' W	25.07.2017	20.04.2018
BE-L9	58° 17.104' N	002° 47.910' W	31.07.2017	
BE-L10	58° 17.724' N	002° 47.698' W	30.07.2017	
BE-M9	58° 17.317' N	002° 46.784' W	27.07.2017	
BE-M10	58° 17.938' N	002° 46.571' W	28.07.2017	

2.2 Installation of Export Cables EC2.2 & EC3

Nexans Norway AS, has completed all export cable installation and burial.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

2.3 Inter Array Cable Pre Lay Grapnel Run (PLGR) & Inter Array Cable Installation

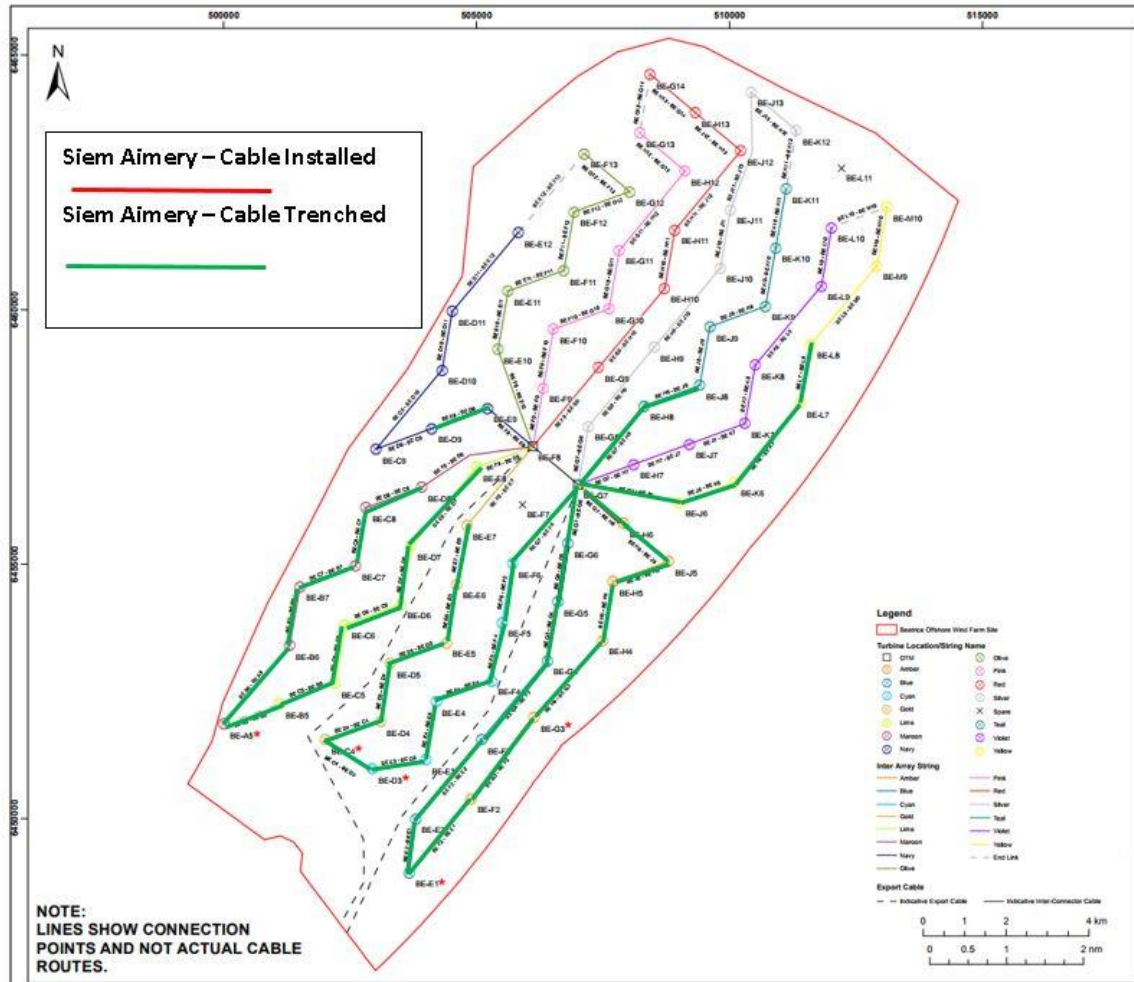


Fig. 3 Cable installation Progress

The CLV Siem Aimery has completed the Inter Array Cables work scope in the second campaign and will return to site around the 19th May to commence the 3rd Inter Array cable installation campaign.

Siem Barracuda is undertaking the following work scopes:

- Personnel transfers to WTG foundations by Ampelmann gangway
- Crane operations to transfer equipment to / from WTG foundations and Offshore Transformer Modules (OTMs).
- Work class ROV activities at the seabed in the vicinity of WTG foundations and OTMs.
- Survey activities along the planned inter-array cable routes linking the appropriate WTG foundations / OTMs.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Installation Sequence	Cable Name	Seabed Route-length m	Latitude Start	Longitude Start	Latitude Finish	Longitude Finish	Cable laid	Cable buried
17	BE-E3-BE-D3	1300.7	58°12.084N	2°55.908W	58°11.99N	2°56.974W	12.03.2018	13.03.2018
18	BE-D3-BE-C4	1419.8	58°12.010N	2°56.975W	58°12.31N	2°57.918W	13.03.2018	13.03.2018
19	BE-E5-BE-D5	1354.3	58°13.327N	2°55.488W	58°13.12N	2°56.615W	20.03.2018	23.03.2018
20	BE-E6-BE-E5	1235.9	58°13.948N	2°55.279W	58°13.34N	2°55.490W	21.03.2018	23.03.2018
21	BE-D4-BE-C4	1253.0	58°12.491N	2°56.821W	58°12.32N	2°57.920W	19.03.2018	20.03.2018
22	BE-D5-BE-D4	1233.6	58°13.112N	2°56.611W	58°12.50N	2°56.824W	26.03.2018	07.04.2018
23	BE-D7-BE-D6	1257.0	58°14.353N	2°56.196W	58°13.744N	°56.406W	21.03.2018	24.03.2018
24	BE-E8-BE-D7	2086.7	58°14.366N	2°56.198W	58°15.189N	2°54.862W	22.03.2018	24.03.2018
25	BE-D6-BE-C6	1300.5	58°13.733N	2°56.405W	58°13.529N	2°57.531W	09.04.2018	10.04.2018
26	BE-C6-BE-C5	1257.8	58°13.517N	2°57.529W	58°12.908N	2°57.740W	09.04.2018	10.04.2018
27	BE-C5-BE-B5	1291.4	58°12.896N	2°57.736W	58°12.693N	2°58.863W	09.04.2018	10.04.2018
28	BE-J7-BE-K7	1291.5	58°15.439N	2°50.574W	58°15.642N	2°49.445W		
29	BE-H7-BE-J7	1289.3	58°15.224N	2°51.698W	58°15.428N	2°50.572W		
30	BE-C8-BE-C7	1231.2	58°14.760N	2°57.110W	58°14.150N	2°57.322W	14.04.2018	28.04.2018
31	BE-C7-BE-B7	1334.5	58°14.139N	2°57.320W	58°13.936N	2°58.445W	10.04.2018	12.04.2018
32	BE-D8-BE-C8	1346.3	58°14.975N	2°55.985W	58°14.772N	2°57.113W	20.04.2018	28.04.2018
33	BE-B7-BE-B6	1232.9	58°13.923N	2°58.443W	58°13.314N	2°58.654W	15.04.2018	
34	BE-K6-BE-L7	2087.5	58°15.033N	2°49.659W	58°15.856N	2°48.319W	15.04.2018	18.04.2018
35	BE-E9-BE-D9	1351.8	58°15.811N	2°54.651W	58°15.609N	2°55.780W	21.04.2018	29.04.2018
36	BE-J6-BE-K6	1301.9	58°14.819N	2°50.784W	58°15.021N	2°49.656W	19.04.2018	
37	OTM1 -BE-H6	1624.4	58°14.995N	2°52.838W	58°14.592N	2°51.907W	17.04.2018	
38	OTM1 -BE-F6	2052.5	58°15.004N	2°52.849W	58°14.175N	2°54.158W	18.04.2018	23.04.2018
39	OTM1 -BE-G6	1261.5	58°14.995N	2°52.841W	58°14.389N	2°53.033W	19.04.2018	23.04.2018
40	OTM2 -BE-E7	2023.3	58°15.403N	2°53.760W	58°14.584N	2°55.075W		
41	OTM2 -BE-E8	1146.7	58°15.412N	2°53.765W	58°15.201N	2°54.865W		
42	BE-H8-BE-J8	1292.3	58°15.846N	2°51.487W	58°16.049N	2°50.359W	21.04.2018	23.04.2018
43	OTM1 -BE-H7	1327.2	58°15.000N	2°52.817W	58°15.213N	2°51.696W		
44	OTM1 -BE-H8	2116.7	58°15.009N	2°52.822W	58°15.834N	2°51.484W	22.04.2018	23.04.2018
45	OTM2 -BE-D8	2375.6	58°15.414N	2°53.766W	58°14.987N	2°55.989W		
46	OTM1 -BE-J6	2320.0	58°14.997N	2°52.820W	58°14.806N	2°50.781W	23.04.2018	01.05.2018
47	OTM2 -BE-E9	1462.4	58°15.407N	2°53.733W	58°16.025N	2°53.526W		
48	BE-L7-BE-L8	1249.0	58°15.868N	2°48.322W	58°16.477N	2°48.108W	24.04.2018	25.04.2018
49	BE-D9-BE-C9	1462.4	58°15.596N	2°55.777W	58°15.381N	2°56.901W		
50	BE-C9-BE-D10	2084.4	58°15.393N	2°56.904W	58°16.214N	2°55.570W		
*Trial 1	BE-A6-BE-B5	~100m	58°12.704N	2°59.391W	58°12.701N	2°59.461W		
*Trial 2	BE-H11-BE-J12	~100m	58°18.042N	2°50.221W	58°18.122N	2°50.085W		
*Trial 3	BE-J11-BE-J13	~150m	58°18.166N	2°49.490W	58°18.217N	2°49.458W		

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

2.4.1 – Vessels involved in activity

On behalf of BOWL, Seaway Heavy Lifting has deployed the Siem Barracuda to carry out the aforementioned works.

CLV Siem Aimery	
General Description and Dimensions:	Length overall 95.3 m Breadth moulded 21.5 m Draft max. 7.2 m
Call Sign:	LATX7
MMSI:	258182000
Onshore Representative:	Majbritt Pauladottir, +47 95 93 60 32, mpa@siemoffshore.com
	

CSV Siem Barracuda	
General Description and Dimensions:	Length overall 121 m Breadth moulded 22 m Draft max. 7 m
Call Sign:	5BZQ3
MMSI:	212253000
Onshore Representative:	Auden Oien + 47 38 600 460 Auden.oien@siemoffshore.com
	

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

2.5 Offshore Transmission Modules (OTM) Commissioning Works

Siemens Transmission and Distribution Ltd (STDL) are carrying out commissioning works on OTM1 and OTM2 in preparation for the energisation of the system.



Fig. 5 OTM1

The Jack-Up vessel, Seajacks Hydra is connected to OTM1 to provide accommodation facilities for OTM1 commissioning.

The Jack-Up vessel, Seajacks Kraken is connected to OTM2 to provide accommodation facilities for OTM2 commissioning.

The walk to work vessel Island Crown is on site as the support and accommodation vessel for works on OTM1 and OTM2.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

2.5.1 – Vessels Involved In Activity

Island Crown	
General Description and Dimensions:	Accommodation and 'Walk to Work' vessel L:96.8m / B:20m
Call Sign:	LACO8
MMSI:	257245000
Onshore Representative:	Project Manager Arnt Petter Osnes T +47 70400025 M +47 46829930 arnt@islandoffshore.com



Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Seajacks Hydra	
General Description and Dimensions:	Jack-Up Accommodation vessel L:76m / B:36m
Call Sign:	3FEI3
MMSI:	370239000
Onshore Representative:	Beatrice Offshore Windfarm Ltd. mc.bowl@sse.com



Seajacks Kraken	
General Description and Dimensions:	Jack-Up Accommodation vessel L:62m / B:36m
Call Sign:	3ESD6
MMSI:	370267000
Onshore Representative:	Beatrice Offshore Windfarm Ltd. mc.bowl@sse.com



Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

2.6 Scientific Equipment Removal & Service and Re-installation

Completed Works

The University of Aberdeen has serviced the moorings listed in Table 1 and reinstalled them in their current locations.

Table 1. Completed mooring service works

Name	As laid coordinates (WGS84 datum)		Characteristics
17	57° 57.759' N	3° 31.260' W	Subsurface with acoustic release.
42	57° 52.337' N	3° 29.058' W	Subsurface with acoustic release.
45	57° 57.261' N	3° 16.084' W	Subsurface with acoustic release.
89	57° 56.056' N	3° 38.252' W	Subsurface with acoustic release.
161	58° 12.933' N	2° 55.954' W	Subsurface with transponder.
164	58° 12.830' N	2° 51.669' W	Subsurface with transponder

The University of Aberdeen has also installed scientific equipment moorings at the locations listed in Table 2.

Table 2. Completed mooring installation works

Name	Coordinates (WGS84 datum)		Characteristics
64	57° 42.521' N	3° 30.174' W	Surface marked (dhan, 12' aluminium & RADAR reflector)
65	57° 43.485' N	3° 25.174' W	Surface marked (dhan, 12' aluminium & RADAR reflector)

Forthcoming Works

The University of Aberdeen intends to service the moorings listed in Table 3 and reinstall them in their current locations.

Table 3. Forthcoming mooring service works

Name	Coordinates (WGS84 datum)		Characteristics
3	58°44.073'N	3°19.776'W	Surface marked (dhan, 12' aluminium & RADAR reflector)
4	57°41.357'N	3°05.547'W	Surface marked (NB50 buoy, red)
160	58°17.648'N	2°49.931'W	Subsurface with transponder
162	58°18.176'N	2°54.124'W	Subsurface with transponder

The moorings listed in Table 4 will be installed.

Table 4. Forthcoming mooring service works

Name	Coordinates (WGS84 datum)		Characteristics
66	57°43.082'N	3°14.977'W	Surface marked (dhan, 12' aluminium & RADAR reflector)
67	57°42.069'N	3°10.026'W	Surface marked (dhan, 12' aluminium & RADAR reflector)

The mooring listed in Table 5 will be removed

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Table 5. Forthcoming mooring removal works

Name	Coordinates (WGS84 datum)		Characteristics
108	58°18.993'N	2°59.223'W	Subsurface

The moorings support sound recording equipment and acoustic loggers that record echolocation clicks of dolphins and porpoises (see images as the foot of this notice) Subsurface moorings fitted with acoustic releases extend no more than three metres vertically from the seabed. Subsurface moorings without acoustic releases extend no more than two metres vertically from the seabed.

Forthcoming works will be subject to weather, and will be carried out by Moray First Marine Ltd using the vessels, Coral Wind or Waterfall.

For information and enquiries please contact: Tim Candido Barton,
Lighthouse Field Station, University of Aberdeen, George St., Cromarty, Ross-shire,
IV11 8YL.

+44 (0)1381 600548.

t.r.barton@abdn.ac.uk



Fig. 6 Examples of equipment which the above moorings support

2.6.1 Vessels Involved In This Operation

Coral Wind	
General Description and Dimensions:	Workboat, UK MCA Cat.2, 60nm from safe haven LOA 14m, Beam 5.1m, Draft 1.2m
Call sign:	2EMX8
MMSI:	235086491
On Board Contact:	Bill Ruck, 07775 802963
E-mail:	bill@moraymarine.com
	

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations

Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

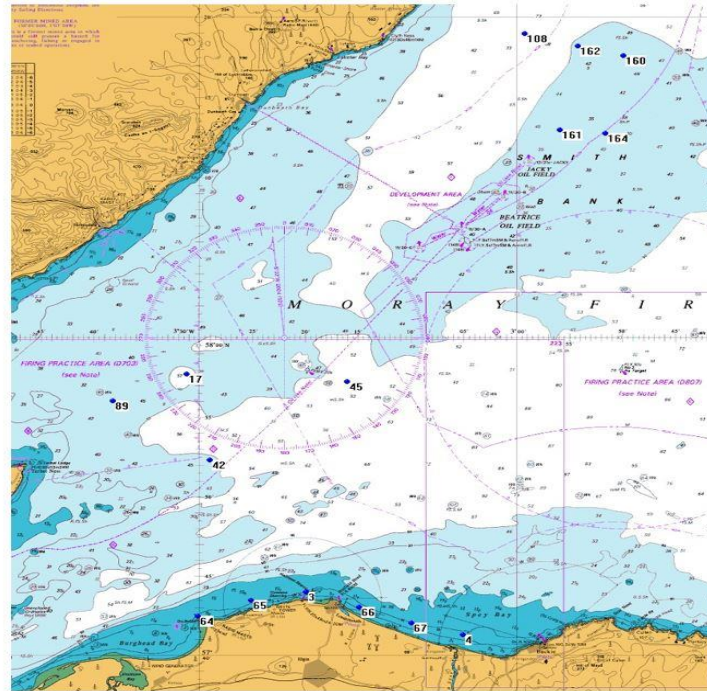


Fig. 7 Scientific equipment locations

3. General Safety Advice

All vessels engaged in the activity will exhibit appropriate lights and shapes prescribed by the International Regulations for Preventing Collisions at Sea; relative to their operations. All vessels engaged in the activity will also transmit an Automatic Identification System (AIS) message.

The Secretary of State has authorised the use of the following safety zones as per Notice to Mariners LF000005-NTM-004.

1. 500 metres radius around each wind turbine, offshore transformer module and / or their substructures and foundations comprising the Beatrice Offshore Wind Farm whilst work is being performed as indicated by the presence of construction vessels.
2. 50 metres radius around each wind turbine, offshore transformer module and / or their substructure and foundations installed but waiting to be commissioned as part of the Beatrice Offshore Wind Farm.

ALL VESSELS ARE REQUESTED to give all construction and support vessels a wide berth.

MARINERS ARE REMINDED to navigate with caution and keep continued watch on VHF Ch. 70 / 16 when navigating the area.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

4. Guard Vessel Deployment

Guard vessels currently on the main construction site are Opportune and Fladda Maid. Artemis is guarding the exposed export cable on behalf of Nexans AS. All vessels can be contacted on VHF Ch.16

Project:	Beatrice Offshore Windfarm Guard Vessel Deployment.
Contractor:	SHL & Nexans – SFF Services Ltd.
Contract Purpose:	Guard Vessel for the Windfarm site.
Area:	BOWL construction site: within the array cable routes and foundation locations. (See Fig 1 for details)
Deployment Dates:	1 st April 2017 – TBC.
Deployment Vessel (s):	Various on a continuous 21 day rotation.
Equipment:	N/A

On behalf of BOWL, Seaway Heavy Lifting has contracted the Scottish Fishermen's Federation (SFF) to provide guard vessels during the piling and foundation installation campaigns. Nexans Norway AS have contracted the SFF to provide guard vessels during the export cable installation campaign. These vessels will change regularly.

The guard vessel's primary duty is security of the construction site by informing and warning non-construction vessels of the ongoing activities and associated Safety Zones

5. Fisheries Liaison

Fisheries liaison associated with the activity will be co-ordinated by Brown and May Marine. For any commercial fishery queries please contact: Alex Winrow-Giffin, telephone: +44 (0)1379 872144 and mobile: +44 (0)7760 160039. alex@brownmay.com

All vessels are to be aware that there has been increased fishing activity close to the BOWL site and vessels may encounter static fishing gear whilst transiting to and from the site. Vessels sheltering to the South and West of the site should pay particular attention and keep a sharp lookout for such static fishing gear. Vessels are reminded that there are recommended transit routes to site, which should help avoid the areas of known fishing activity.

6. Distribution List

The distribution of this notice is as per email recipient's header. A central list of recipients is maintained by the Marine Coordinator. If you are not the appropriate recipient of these notices, or do not wish to receive the notices in the future, please contact us at the address included in Section 1 of this notice.

7. Website

The official website of Beatrice Offshore Windfarm Limited can be found at:

<https://www.beatricewind.com>

This contains all Notices to Mariners (NtM) published by BOWL and all Weekly Notices of Operations, together with a large amount of general information about the Project.

There is also a Twitter feed at <https://twitter.com/beatricewind>.

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018
LF000005-WNO-013: Weekly Notice of Operations - Rev 54

Beatrice Offshore Windfarm
Vessels & Operators

Reference to Marine Licence
Conditions 2.5, 2.6 and 3.1.2

Vessel Data Matrix OWF



No Ref	Vessel Picture	Vessel Name / Flag	Type / Function	Operator	Contact / contact details	Call sign / MMSI / IMO	LOA (m) Beam (m) Draft (m)	Date on Site	Marine Licence applicable
1		Smit Sentosa	Anchor Handling Tug	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/o Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire AB32 6FE +31 653997158 EMAIL:dsprangers@shl.nl	ORRX / 205696000 IMO9662356	51.8 x 15.0 x 6.2m	01.01.2018	OWF
2		Seajacks Hydra	Jack Up Accodation Vessel	Seajacks	BOWI Offshore Windfarm Ltd. mc.bowl@sse.com	3FEI3 / 370239000	62 x 36 m	15.04.2018	OWF & OFTW
3		Smit Seraga	Barge Tow Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/o Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire AB32 6FE +31 653997158 EMAIL:dsprangers@shl.nl	9Y9845 / 566804000 IMO9662368	51.8 x 16 x 6m	01.01.2018	OWF
4		Island Crown	Walk to work OTM commissioning	Stålhaugen 12, 6065 Ulsteinvik, Norway +47 70400000	Project Manager Arnt Petter Osnes T +47 70400025 M +47 46829930 arnt@islandoffshore.com	LAC08/9630535 IMO257245000	96 x 20 m	01.02.2017	OWF & OFTW
5		Seajacks Kraken	Jack Up Accodation Vessel	Seajacks	BOWI Offshore Windfarm Ltd. mc.bowl@sse.com	3ESD6 / 370267000	62 X 36 m	08.05.2018	OWF & OFTW
6		Rix Lion	Crew Transfer Vessel / CTV	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/o Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire AB32 6FE +31 653997158 EMAIL:dsprangers@shl.nl	2HOH3 / 235105282	26 x 10 x 2.5m	06.04.2018	OWF
7		Kamarina	Barge Tow Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	IITW2 / 247278400 IMO9499644	50 x 15m	08.08.2017	OWF

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

9		Opportune WK171	Guard Vessel	Scottish Fishermens Federation (SFF) for Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	2VKH/ 233608006	26 x 7m	30.04.2018	OWF
10		Rix Panther	Crew Transfer Vessel / CTV	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	2FRT9/ 233093688	19 x 8m	04.05.2018	OWF
11		DSV Aramis	Dive Support Vessel	Nexans Norway AS Innsporten 9, 0663 Oslo, Norway +47 22 88 61 00	Oyvind Haug BOWL Installation Engineering Manager Mob +47 916 27 674 Office +47 22886509	N/A	15 x 5m	23.03.2018	OFTW
12		DSV Athos	Dive Support Vessel	Nexans Norway AS Innsporten 9, 0663 Oslo, Norway +47 22 88 61 00	Oyvind Haug BOWL Installation Engineering Manager Mob +47 916 27 674 Office +47 22886509	N/A	5 x 2m	23.03.2018	OFTW
13		Seacat Intrepid	Crew Transfer Vessel / CTV	Seacat Services Ltd	Lea Hurst Marine Manager, Seacat Services Ltd 2 Mariners Way, Cowes, Isle of Wight +44 (0)1983 475315 lea.hurst@seacatservices.co.uk	2HWU6 / 235107284	27 x 10 x 1.5m	25.09.2017	OWF & OFTW
14		Morning Dawn PD359	Guard Vessel	Scottish Fishermens Federation (SFF) for Nexans AS	Oyvind Haug BEATRICE Installation Engineering Manager Mob: +47 916 27 674 Office: +47 22 88 65 09	MHEU3 / 232253000	45 x 9 m	21.11.2017	OWF & OFTW
15		Fladda Maid	Guard Vessel	Scottish Fishermens Federation (SFF) for SHL	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	MHXX6 / 233826000	20 x 7m	08/05/2018	OWF & OFTW

Weekly Notice of Operations (WNoO)

Beatrice Offshore Windfarm Limited

Construction Operations



Issue Date: 14th May 2018

LF000005-WNO-013: Weekly Notice of Operations - Rev 54

16		Fairplay 33	Barge Tow Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	Y2QG6 / 305356000	48.8 x 14 x 6.2m	15/04/2018	OWF
17		Maersk Trader	Supply Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	220584000 / OXRO2	73m x 20m	12/04/2018	OWF
18		Oleg Strashnov	Heavy Lift Vessel / HLV	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	5BNL2 / 212905000	183.3 x 47 x 13.5	08.08.2017	OWF & OffW
19		Yos Prelude	Supply Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	2WKH/ 233608006	74m x 16m	16/11/2017	OWF
20		Bremen Fighter	Barge Tow Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	Y20Y1 / 304742000	48.1 x 14.06 x 6.0m	14.12.2017	OWF
21		Britoil 120	Barge Tow Vessel	Seaway Heavy Lifting (SHL)	Danny Sprangers (SHL) C/O Subsea 7 East Campus Arnhall Business Park Westhill, Aberdeenshire, AB32 6FE +31 653997158 Email - dsprangers@shl.nl	9Y7116 / 564104000	59m x 16m	09.03.2018	OWF
